

South 154th Street Improvements

City of SeaTac

Final Acceptance

February 12, 2013




Project Elements

- **Sidewalks, Curb & Gutter**
- **Undergrounding of Overhead Utilities**
- **New Pavement / Overlay / Channelization**
- **Landscaping, Fencing and Retaining Walls**
- **Drainage System**
 - Detention Vaults
 - Water Quality vaults



Location

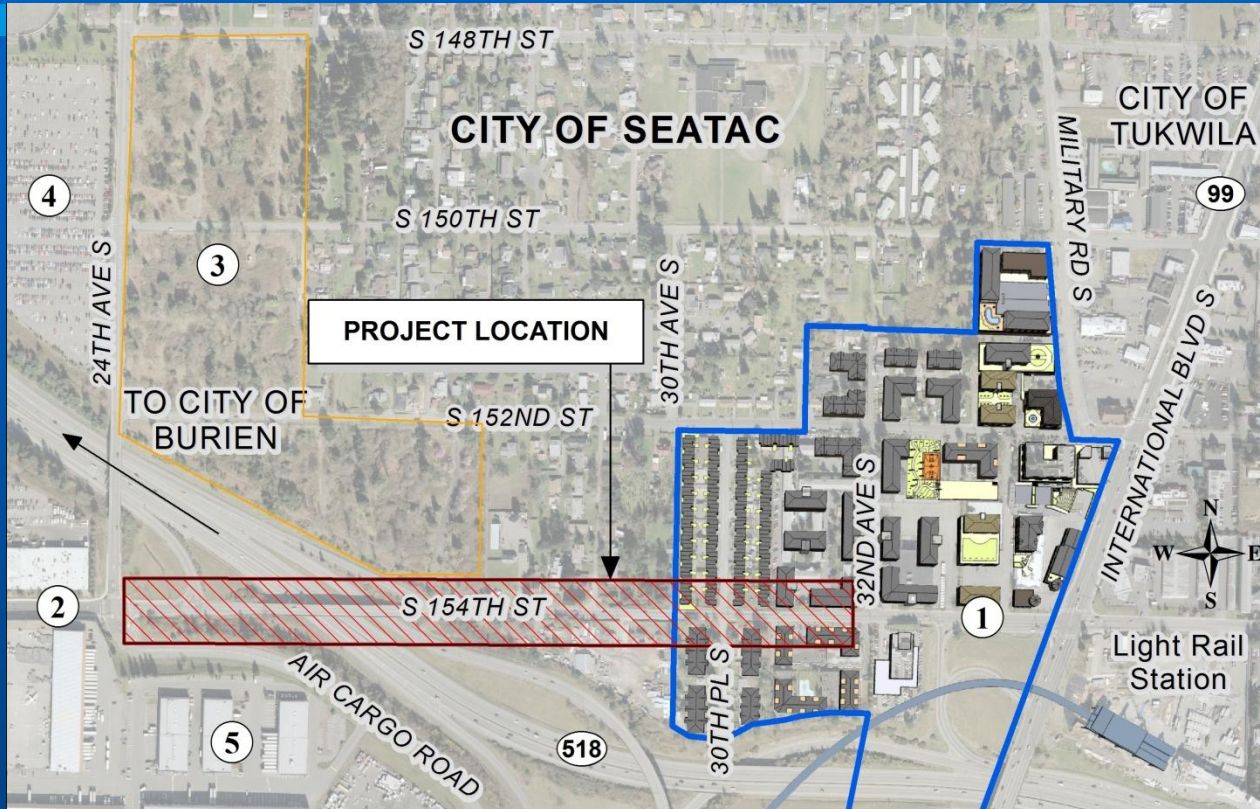

City of SeaTac

0 300 600 Feet

Date Prepared: March 24, 2009

 Project Location

 SeaTac Urban Center


- ① Street Improvements by Sound Transit (2009)
- ② Street Improvements by Port of Seattle (2006)
- ③ Future North Freight Cargo Complex
- ④ Port of Seattle Staff Parking
- ⑤ Port of Seattle Cargo Complex



S 154th St Looking East



S 154th St, Southside Looking West from SR 518 Bridge

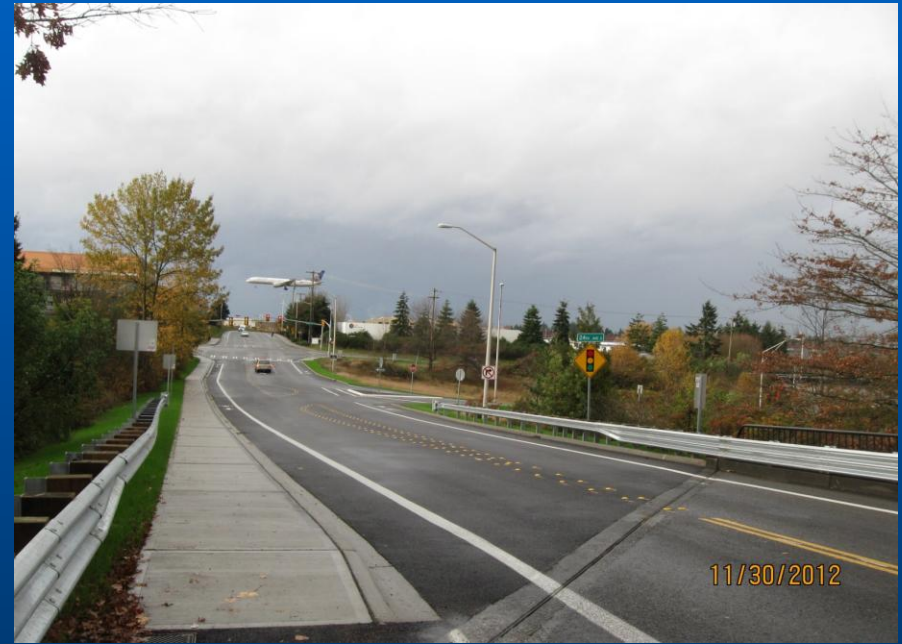

S 154th St, North Side Looking East



Expenditures

	<u>Authorized</u>	<u>Actual</u>
Construction Contract	\$4,216,708	\$4,216,708
Contingency	\$421,671	\$339,766
Materials Testing	\$20,000	\$29,752
WSDOT Bridge Inspection		\$20,197
Inspector Overtime	\$15,000	\$12,638
Seattle City Light Conversion	600,000	575,448
Total	\$5,273,378	\$5,194,509



Funding

	<u>Authorized</u>	<u>Actual</u>
Federal Aid Grant	\$1,500,000	\$1,500,000
TIB Grant	\$2,170,800	\$2,170,800
Water District 125 Reimbursement	\$48,508	\$76,075
Comcast Reimbursement	\$14,080	\$19,531
Valley View Sewer District		\$1,209
Century Link Reimbursement		\$11,673
City 307 Fund	\$1,539,990	\$1,415,221
Total	\$5,273,378	\$5,194,509

