

South 164th Street Sidewalk Improvements

City of SeaTac

Final Acceptance

**February 12, 2013 Council
Study Session**



Project Elements


- **Sidewalks, Curb & Gutter**
- **Pavement Resurfacing**
- **Fencing and Retaining Walls**
- **Drainage System**
 - **Pervious Concrete Sidewalks**
 - **Conveyance System**




S 164th St, South Side Looking East from 34th Ave S



S 164th St , North Side Looking West

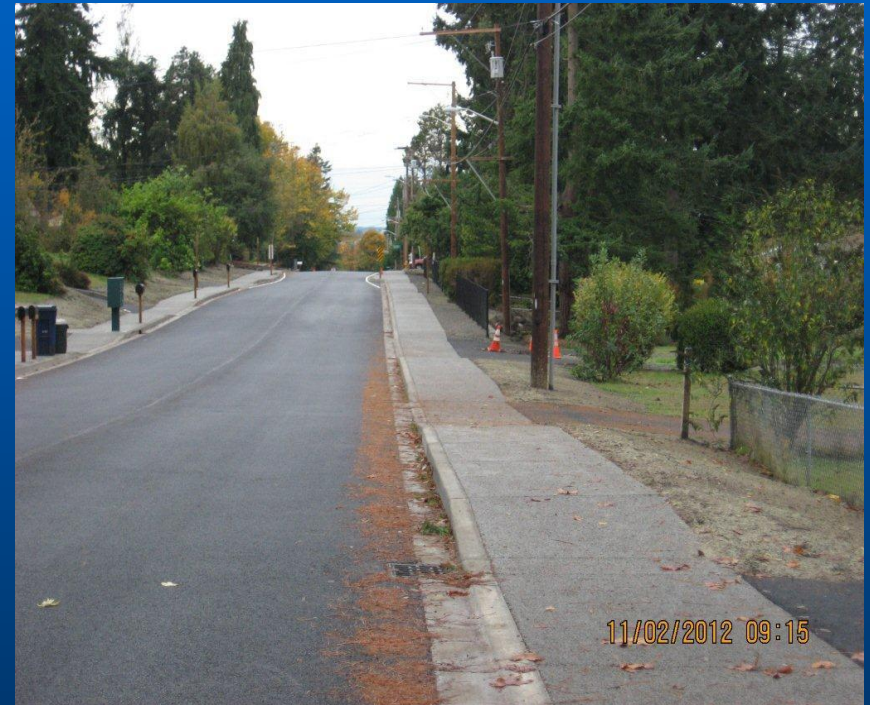

S 164th St, South Side Looking East

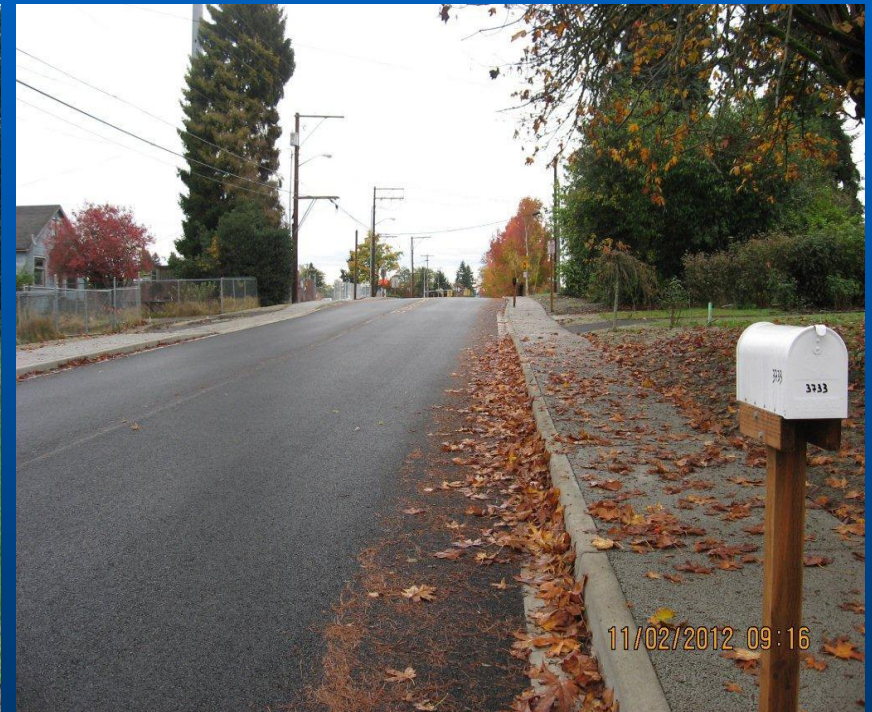

Expenditures

	<u>Authorized</u>	<u>Actual</u>
Construction Contract	\$893,727	\$695,798
Contingency	89,373	0
Materials Testing	10,000	1,054
Inspector Overtime	<u>10,000</u>	<u>1,013</u>
Total	\$1,003,100	\$697,865



Funding

	<u>Authorized</u>	<u>Actual</u>
City 307 Transportation Fund	<u>1,003,100</u>	<u>697,965</u>
Total	\$1,003,100	\$697,865



Neighborhood Sidewalk Program

- Residential, non-arterial
- 20 years
- 12.5 miles
- ~\$1.5m/year = \$36.1m



Neighborhood Sidewalk Program

- 3 Projects Complete
- \$3.5m
- 1.4miles



Sidewalks in SeaTac

Pre-Cityhood	=	10.7 miles
Built	=	<u>32.5</u>
Total		43.2 miles

